

## PLANNED TREE MAINTENANCE

|                                                                     |  |                           |                        |
|---------------------------------------------------------------------|--|---------------------------|------------------------|
| <b>Tree Works Notification</b>                                      |  | <b>Created By:</b>        |                        |
| <b>Public Scrutiny</b>                                              |  | <b>Date:</b>              |                        |
| <b>Tree Works reference number and schedule title</b>               |  |                           |                        |
|                                                                     |  |                           |                        |
| <b>Wards included within planned works:</b>                         |  |                           |                        |
| Abbey                                                               |  | East Chesterton           | Queen Ediths           |
| Arbury                                                              |  | Kings Hedges              | Romsey                 |
| Castle                                                              |  | Market                    | Trumpington            |
| Cherry Hinton                                                       |  | Newnham                   | West Chesterton        |
| Coleridge                                                           |  | Petersfield               |                        |
| <b>Within following Council service areas:</b>                      |  |                           |                        |
| Highways                                                            |  | Housing                   | Parks                  |
| <b>Size of schedule – based on number of trees included within:</b> |  |                           |                        |
| Small<br>( < 10 trees)                                              |  | Medium<br>(11 - 50 trees) | Large<br>( > 50 trees) |
| <b>Brief description of the works</b>                               |  |                           |                        |
|                                                                     |  |                           |                        |

## **Tree Works Notification**

For tree works submitted under a 'Tree Works Notification' I refer you to Policy GM3 of the Cambridge City Council Citywide Tree Strategy 2016-2026 Part 2:

*"All planned tree works will be published on the Council website and through site notices for the community to access at least 20 working days before implementation. The council sees this as an important tool for communicating to the local community about tree work planned for their area and the reasons why the works are necessary."* <https://www.cambridge.gov.uk/tree-strategy>

The notification period will run for 20 days from the date of publication of the schedule.

The majority of the works contained within these schedules consists of minor pruning to address health and safety issues, or more significant works to remove trees that are obviously dead, dying or diseased, or replacement planting for trees that have been removed.

A brief outline of the planned works can be found in the table shown above however; full details of the planned works can be found within the attached schedules and maps.

Please note: where trees are due to be felled, these are marked on site with green tape.

## **Public Scrutiny**

For tree works submitted for 'Public Scrutiny' A brief outline of the planned works which we wish to be publicly scrutinised can be found within the attached schedules and maps which will be available for ten working days following the date of publication.

The planned works could involve either removing healthy trees over 75mm in diameter as measured at 1.5m above ground level and/or any tree work or batch of works that will have a significant impact on the landscape character of an area as assessed by an arboricultural officer. This will include crown reductions of over 30% in branch length on trees that have not previously been reduced.

The table above provides details of the works which are open for public scrutiny, please note that some tree works schedules may contain other works in other service areas than those open to this level of scrutiny. The following details only relate to the significant works considered for scrutiny. Please note: where trees are

due to be felled, these are clearly marked on site with green tape.

I refer you to Policy GM5 of the Cambridge City Council [Citywide Tree Strategy 2016-2026 Part 2](#):

*“When considering tree works on City Council land, the Council will invite resident and stakeholder comment regarding the following kinds of work:*

- a) Any tree work which will have a significant impact on the character of an area.*
- b) Felling healthy trees of over 75mm diameter”*

If you wish to make a comment about any of the works proposed, please submit them via this link: [Comment on a tree work schedule](#). All unresolved objections to tree work subject to public scrutiny will be determined by the relevant Executive Councillor.

Location:

LW0 August 25

Site type:

Order no/ref:  
Contract/Client Ref:  
Item created: 01 October 2025

Priority of works:  
Start on/after:  
Complete by:

| Tree/Item code | Species/Work required | Rate | Quantity | Cost |
|----------------|-----------------------|------|----------|------|
|----------------|-----------------------|------|----------|------|

Brooks Road Play Area (BROOKU), Romsey

|                |                                                                                                        |  |          |  |
|----------------|--------------------------------------------------------------------------------------------------------|--|----------|--|
| Grp/2 (360272) | Hazel (Common) (Corylus avellana) (///comet.fake.hurls)                                                |  |          |  |
| \$WR           | Recommended Works - see Comments (x 10 tree) - trim and cut back face of hedge beside 117 brooks road. |  | 10 trees |  |

Cambridge Community Orchard (CCO), Trumpington

|                  |                                                                                                           |  |        |  |
|------------------|-----------------------------------------------------------------------------------------------------------|--|--------|--|
| Sgl/169 (535758) | Prunus (Wild Cherry) (Prunus avium) (///rope.garden.onion)                                                |  |        |  |
| RT1              | Remove tree leaving 1m high stump marked with red paint. you can leave stumps taller than 1m for habitat. |  | 1 tree |  |
| Sgl/170 (535759) | Prunus (Wild Cherry) (Prunus avium) (///hook.curving.verbs)                                               |  |        |  |
| RT1              | Remove tree leaving 1m high stump marked with red paint. you can leave stumps taller than 1m for habitat. |  | 1 tree |  |
| Sgl/171 (535761) | Prunus (Wild Cherry) (Prunus avium) (///waters.stays.ladder)                                              |  |        |  |
| RT1              | Remove tree leaving 1m high stump marked with red paint. you can leave stumps taller than 1m for habitat. |  | 1 tree |  |
| Sgl/172 (535762) | Prunus (Wild Cherry) (Prunus avium) (///sparks.full.tribes)                                               |  |        |  |
| RT1              | Remove tree leaving 1m high stump marked with red paint. you can leave stumps taller than 1m for habitat. |  | 1 tree |  |
| Sgl/173 (535763) | Prunus (Wild Cherry) (Prunus avium) (///elbow.tiles.image)                                                |  |        |  |
| RT1              | Remove tree leaving 1m high stump marked with red paint. you can leave stumps taller than 1m for habitat. |  | 1 tree |  |
| Sgl/174 (535765) | Prunus (Wild Cherry) (Prunus avium) (///curry.first.staple)                                               |  |        |  |
| RT1              | Remove tree leaving 1m high stump marked with red paint. you can leave stumps taller than 1m for habitat. |  | 1 tree |  |
| Sgl/175 (535766) | Prunus (Wild Cherry) (Prunus avium) (///wasp.trip.crew)                                                   |  |        |  |
| RT1              | Remove tree leaving 1m high stump marked with red paint. you can leave stumps taller than 1m for habitat. |  | 1 tree |  |

| Tree/Item code                                         | Species/Work required                                                                                                 | Rate | Quantity | Cost |
|--------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------|------|----------|------|
| Sgl/176 (535767)                                       | Prunus (Wild Cherry) (Prunus avium) (///trend.soccer.fire)                                                            |      |          |      |
| RT1                                                    | Remove tree leaving 1m high stump marked with red paint. you can leave stumps taller than 1m for habitat.             |      | 1 tree   |      |
| Campkin Road (CAMPKR), Kings Hedges                    |                                                                                                                       |      |          |      |
| Sgl/138 (222656)                                       | Ailanthus (Tree of Heaven) (Ailanthus altissima) o/s 68 (///music.moon.expect)                                        |      |          |      |
| CRW                                                    | C/R - to clear BT wire by 0.5m                                                                                        |      | 1 tree   | 0.00 |
| RDW                                                    | Rem - deadwood                                                                                                        |      | 1 tree   | 0.00 |
| Carlton Way (CARLTW), West Chesterton                  |                                                                                                                       |      |          |      |
| Sgl/8 (083108)                                         | Alder (Italian) (Alnus cordata) o/s 44/46 (///chained.sleep.catch)                                                    |      |          |      |
| \$WR                                                   | Recommended Works - see Comments - Reduce height of the two main side stems by 4-5m. leave central leader.            |      | 1 tree   |      |
| Ditton Fields (DITTOF), Abbey                          |                                                                                                                       |      |          |      |
| Sgl/90 (011864)                                        | Birch (Silver) (Betula pendula) o/s 293 (///frozen.rates.insist)                                                      |      |          |      |
| RFR                                                    | Rem - tree for replant                                                                                                |      | 1 tree   | 0.00 |
| Foster Road Allotments (FOSALT), Trumpington           |                                                                                                                       |      |          |      |
| Sgl/13 (532400)                                        | Walnut (Common) (Juglans regia) foster rd (///lamps.cigar.focus)                                                      |      |          |      |
| CLT                                                    | C/L - to over allotment by 5m                                                                                         |      | 1 tree   | 0.00 |
| CRS                                                    | C/R - sides by Reduce overhang of allotment by pruning ends of branch by 1-2 m or back to previous points.            |      | 1 tree   | 0.00 |
| Sgl/24 (980013)                                        | Leyland Cypress (Common) (x Cupressocyparis leylandii) (///finishing.burns.angel)                                     |      |          |      |
| RHG                                                    | Remove - lodging branch remove split and broken branches in Lower crown both over greenhouse and top of chicken sheds |      | 1 tree   | 0.00 |
| High Street, East Chesterton (HIGHSE), East Chesterton |                                                                                                                       |      |          |      |
| Sgl/6 (045468)                                         | Lime (American Cv.) (Tilia americana 'American Sentry') opp 92 (///hidden.pies.could)                                 |      |          |      |
| \$WR                                                   | Recommended Works - see Comments - Remove lowest branch on roadside, into mainstem.                                   |      | 1 tree   |      |

| Tree/Item code                               | Species/Work required                                                                                     | Rate | Quantity | Cost |
|----------------------------------------------|-----------------------------------------------------------------------------------------------------------|------|----------|------|
| Sgl/10 (045484)                              | Lime (Unspecified) (Tilia species) o/s 175 (///jungle.frost.supply)                                       |      |          |      |
| \$WR                                         | Recommended Works - see Comments - lift to approx 3m over pavement.                                       |      | 1 tree   |      |
|                                              | - Remove vehicle damaged limbs over roadside. prune in side branches into scaffold branches as necessary. |      |          |      |
| Sgl/11 (045488)                              | Lime (Unspecified) (Tilia species) o/s 183 (///hiding.courier.priced)                                     |      |          |      |
| \$WR                                         | Recommended Works - see Comments - lift to approx 3m over pavement.                                       |      | 1 tree   |      |
|                                              | - Remove vehicle damaged limbs over roadside. prune in side branches into scaffold branches as necessary. |      |          |      |
| Sgl/12 (045492)                              | Lime (Unspecified) (Tilia species) o/s 193 (///gears.grape.next)                                          |      |          |      |
| \$WR                                         | Recommended Works - see Comments - lift to approx 3m over pavement.                                       |      | 1 tree   |      |
|                                              | - Remove stem epi.                                                                                        |      |          |      |
|                                              | - Remove vehicle damaged limbs over roadside. prune in side branches into scaffold branches as necessary. |      |          |      |
| Jack Warren Green Growth Site (JWGGS), Abbey |                                                                                                           |      |          |      |
| Sgl/13 (525616)                              | Lime (Common) (Tilia x europaea) (///unhappy.dragging.quilting)                                           |      |          |      |
| CLF                                          | C/L - over footpath to 2.4m                                                                               |      | 1 tree   | 0.00 |
| Sgl/23 (529421)                              | Ash (Common) (Fraxinus excelsior) (///archive.embellish.forms)                                            |      |          |      |
| CLF                                          | C/L - over footpath to 2.4m                                                                               |      | 1 tree   | 0.00 |
| Kings Hedges Road (KINGSH), Kings Hedges     |                                                                                                           |      |          |      |
| Sgl/12 (227212)                              | Apple (Japanese Crab) (Malus x floribunda) o/s 35/37 (///pure.heat.cared)                                 |      |          |      |
| RFR                                          | Rem - tree for replant                                                                                    |      | 1 tree   | 0.00 |
| Monkswell (MONKSW), Trumpington              |                                                                                                           |      |          |      |
| Sgl/67 (386453)                              | Ash (Common) (Fraxinus excelsior) in drainage ditch (///forest.sooner.useful)                             |      |          |      |
| \$WR                                         | Recommended Works - see Comments - Remove large low limbs over washing area, into mainstem.               |      | 1 tree   |      |

| Tree/Item code | Species/Work required | Rate | Quantity | Cost |
|----------------|-----------------------|------|----------|------|
|----------------|-----------------------|------|----------|------|

Perne Road (PERNER), Coleridge

|                 |                                                                                                     |  |        |      |
|-----------------|-----------------------------------------------------------------------------------------------------|--|--------|------|
| Sgl/33 (186040) | Ash (Common) (Fraxinus excelsior) o/s 71-73 (///pops.noises.liability)                              |  |        |      |
| CL5             | Crown lift to 5m - lift to approx gutter height, taking branches into side branches.                |  | 1 tree |      |
| CRB             | C/R - to clear building by - prune back from front of houses to create 4-5m between tree and house. |  | 1 tree | 0.00 |
| Sgl/36 (186044) | Ailanthus (Tree of Heaven) (Ailanthus altissima) o/s 83-85 (///gross.supply.burst)                  |  |        |      |
| CL5             | Crown lift to 5m - lift to approx gutter height.                                                    |  | 1 tree |      |
| CRB             | C/R - to clear building by achieve 5m gap between tree and building.                                |  | 1 tree | 0.00 |

Peverel Close (PEVERC), Abbey

|                 |                                                                                       |  |        |      |
|-----------------|---------------------------------------------------------------------------------------|--|--------|------|
| Sgl/31 (004316) | Ash (Raywood / Claret) (Fraxinus angustifolia 'Raywood') 01842 (///daisy.cafe.prefer) |  |        |      |
| RDW             | Rem - deadwood - large piece going towards horse chestnut                             |  | 1 tree | 0.00 |

Red Cross Lane (REDCRO), Queen Ediths

|                |                                                               |  |        |      |
|----------------|---------------------------------------------------------------|--|--------|------|
| Sgl/2 (328804) | Oak (Turkey) (Quercus cerris) o/s 24 (///shared.dated.motion) |  |        |      |
| CLD            | C/L - over drive to - 6-7M.                                   |  | 1 tree | 0.00 |

Sheeps Green North (COEFEN), Newnham

|                 |                                                                                      |  |        |      |
|-----------------|--------------------------------------------------------------------------------------|--|--------|------|
| Sgl/95 (509536) | Willow (Golden Weeping) (Salix x sepulcralis var. chrysocoma) (///trader.rots.stuck) |  |        |      |
| \$WR            | Recommended Works - see Comments remove fallen branch from watercourse               |  | 1 tree |      |
| CRX             | C/R - to previous reduction points                                                   |  | 1 tree | 0.00 |

Teversham Drift (TEVERE), Cherry Hinton

|                 |                                                                        |  |        |      |
|-----------------|------------------------------------------------------------------------|--|--------|------|
| Sgl/51 (152404) | Prunus (Wild Cherry) (Prunus avium) grass o/s 31 (///asks.chains.rent) |  |        |      |
| RFR             | Rem - tree for replant                                                 |  | 1 tree | 0.00 |

| Tree/Item code | Species/Work required | Rate | Quantity | Cost |
|----------------|-----------------------|------|----------|------|
|----------------|-----------------------|------|----------|------|

Woodlark Road (WOODLR), Castle

Sgl/12 (125840) Amelanchier (Serviceberry) (Amelanchier laevis) o/s 37/39  
(///fees.bumpy.pipe)

RFR Rem - tree for replant 1 tree 0.00

Expenditure code analysis :-

Expenditure code not specified

Schedule item analysis :-

|     |                                    |                |
|-----|------------------------------------|----------------|
| CLD | C/L - over drive to                | 1 tree @ 0.00  |
| CLF | C/L - over footpath to 2.4m        | 2 trees @ 0.00 |
| CLT | C/L - to                           | 1 tree @ 0.00  |
| CRB | C/R - to clear building by         | 2 trees @ 0.00 |
| CRS | C/R - sides by                     | 1 tree @ 0.00  |
| CRW | C/R - to clear BT wire by 0.5m     | 1 tree @ 0.00  |
| CRX | C/R - to previous reduction points | 1 tree @ 0.00  |
| RDW | Rem - deadwood                     | 2 trees @ 0.00 |
| RFR | Rem - tree for replant             | 4 trees @ 0.00 |
| RHG | Remove - lodging branch            | 1 tree @ 0.00  |

Contractor:

Total cost: 0.00

Issued by:

Kenny McGegeor



ARBORICULTURAL WORKS ORDER

Item Ref: 02470

LW0 August 25




Brooks Road Play Area (BROOKU), Romsey



ARBORICULTURAL WORKS ORDER

Item Ref: 02470


Cambridge Community Orchard (CCO), Trump

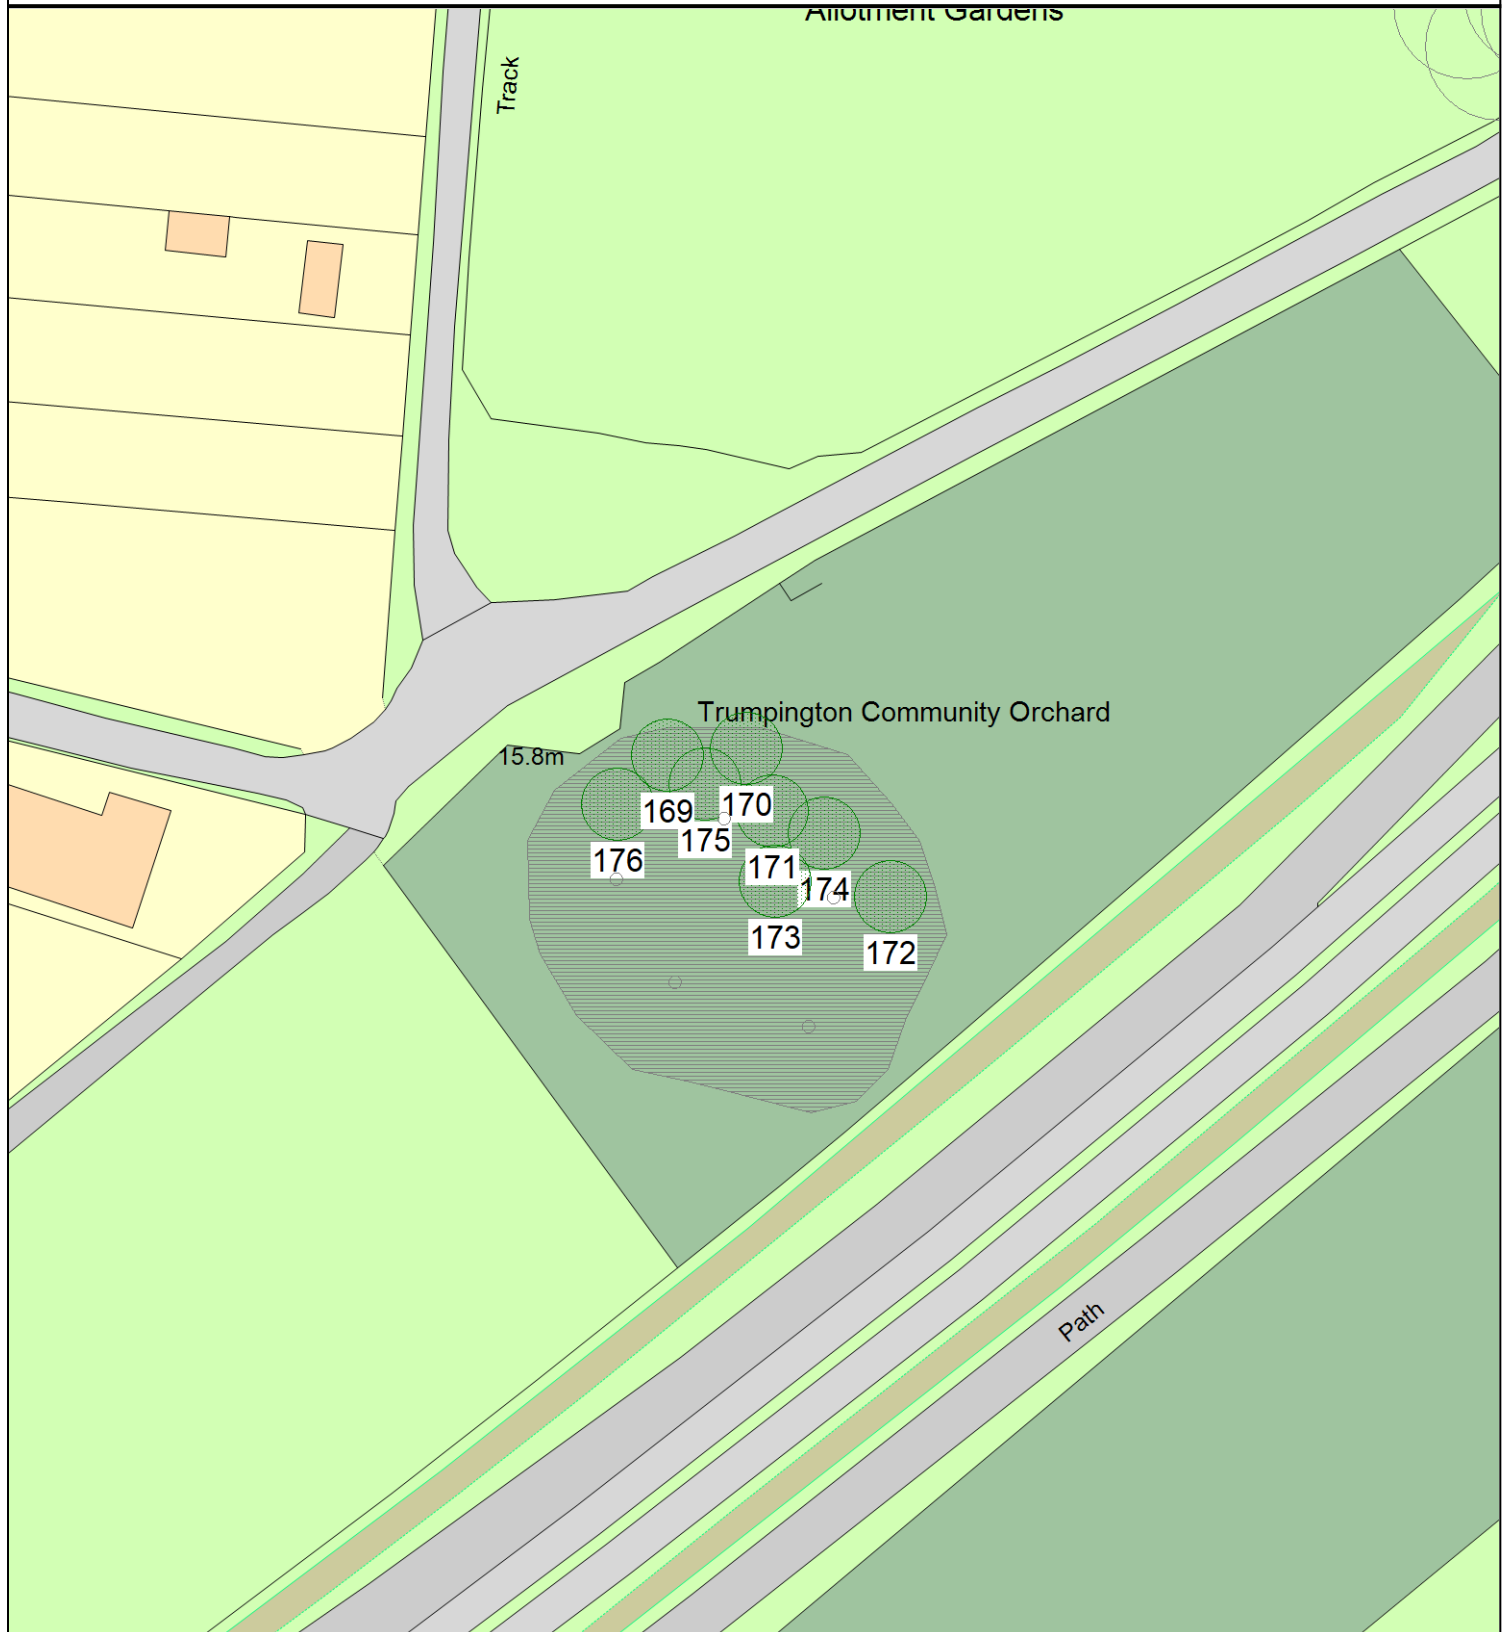

ARBORICULTURAL WORKS ORDER

Item Ref: 02470

Campkin Road (CAMPKR), Kings Hedges

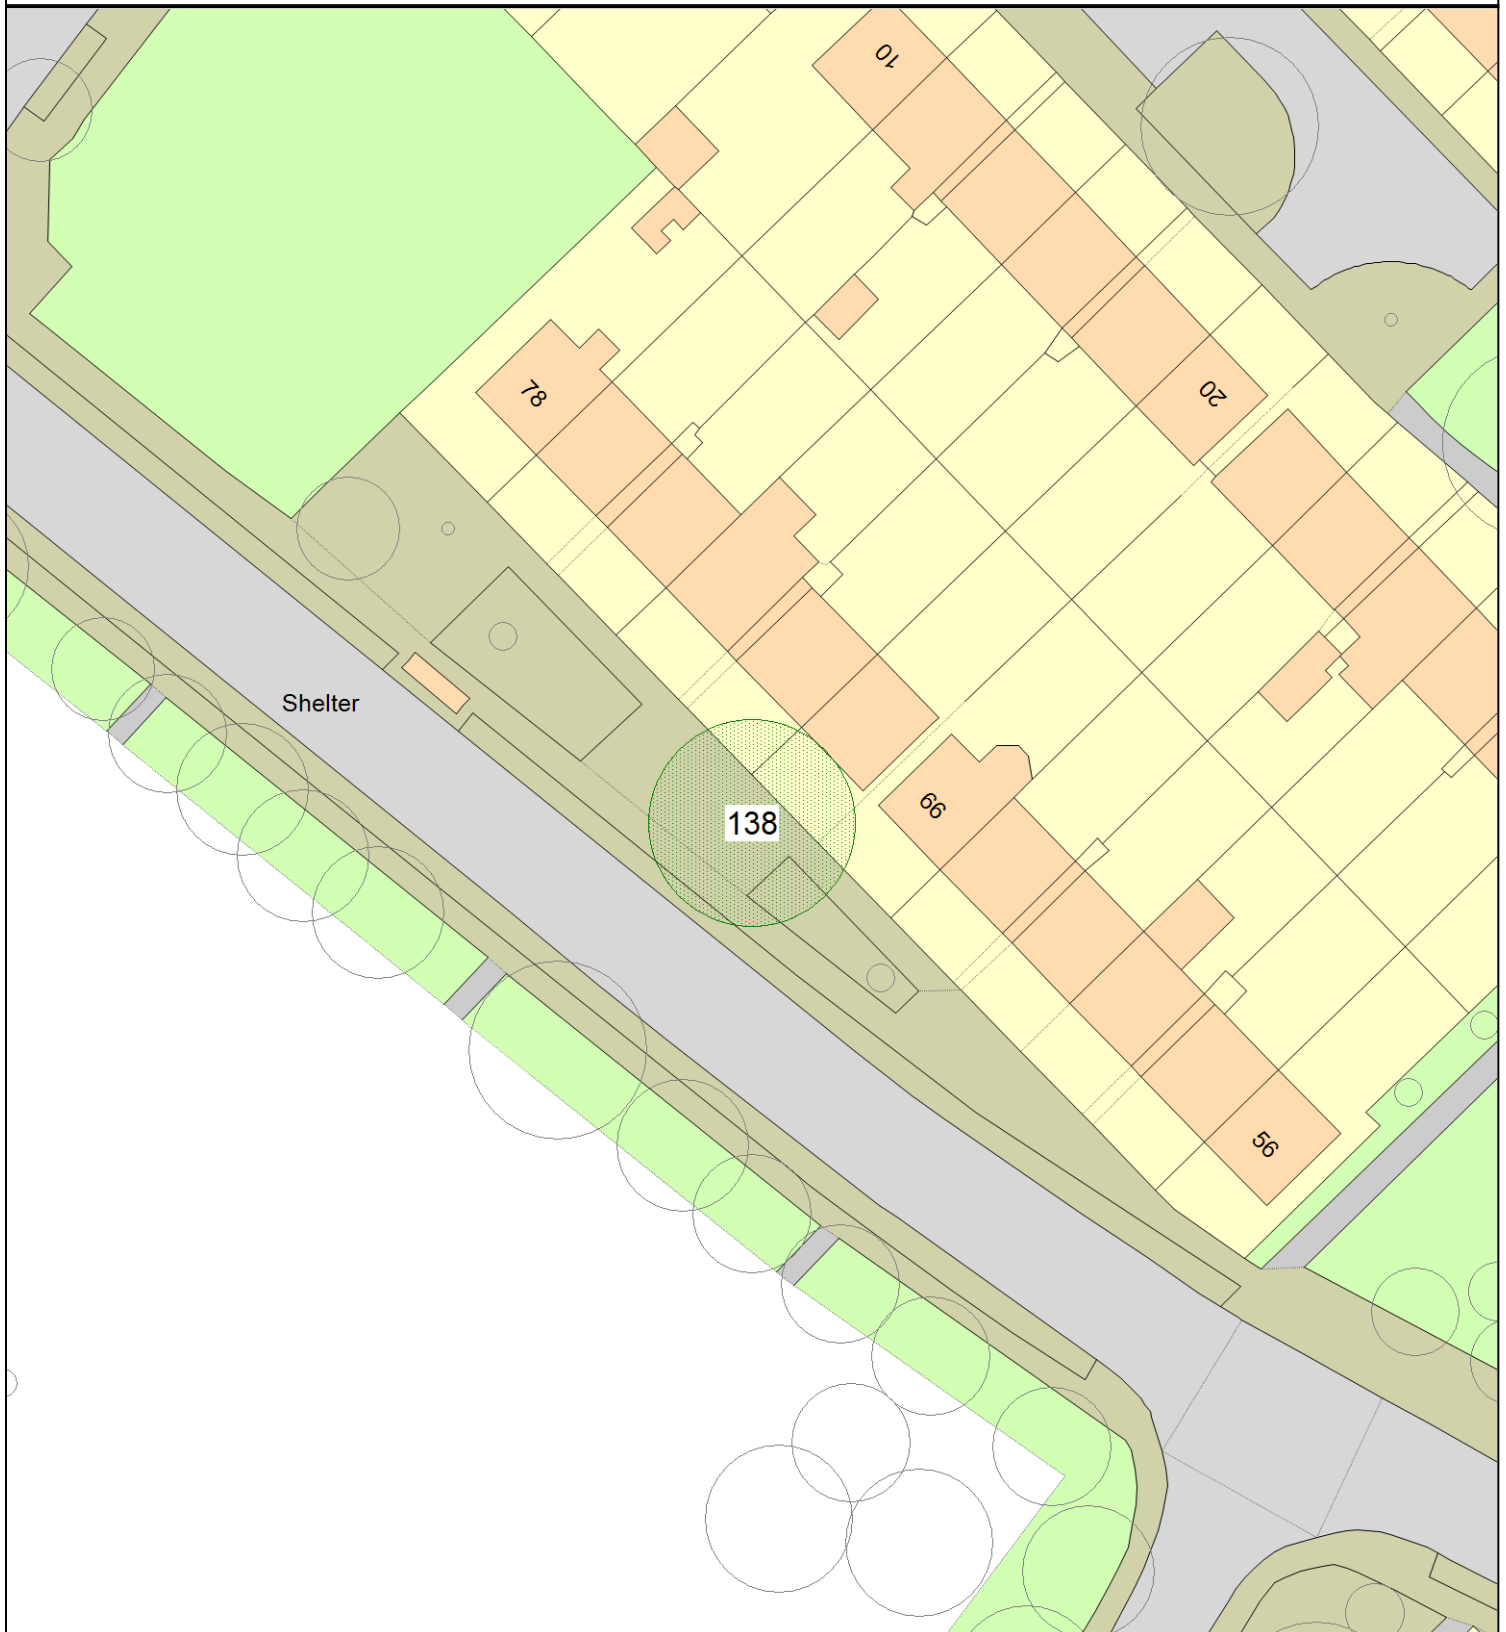

ARBORICULTURAL WORKS ORDER

Item Ref: 02470


Carlton Way (CARLTW), West Chesterton



ARBORICULTURAL WORKS ORDER

Item Ref: 02470

Ditton Fields (DITTOF), Abbey

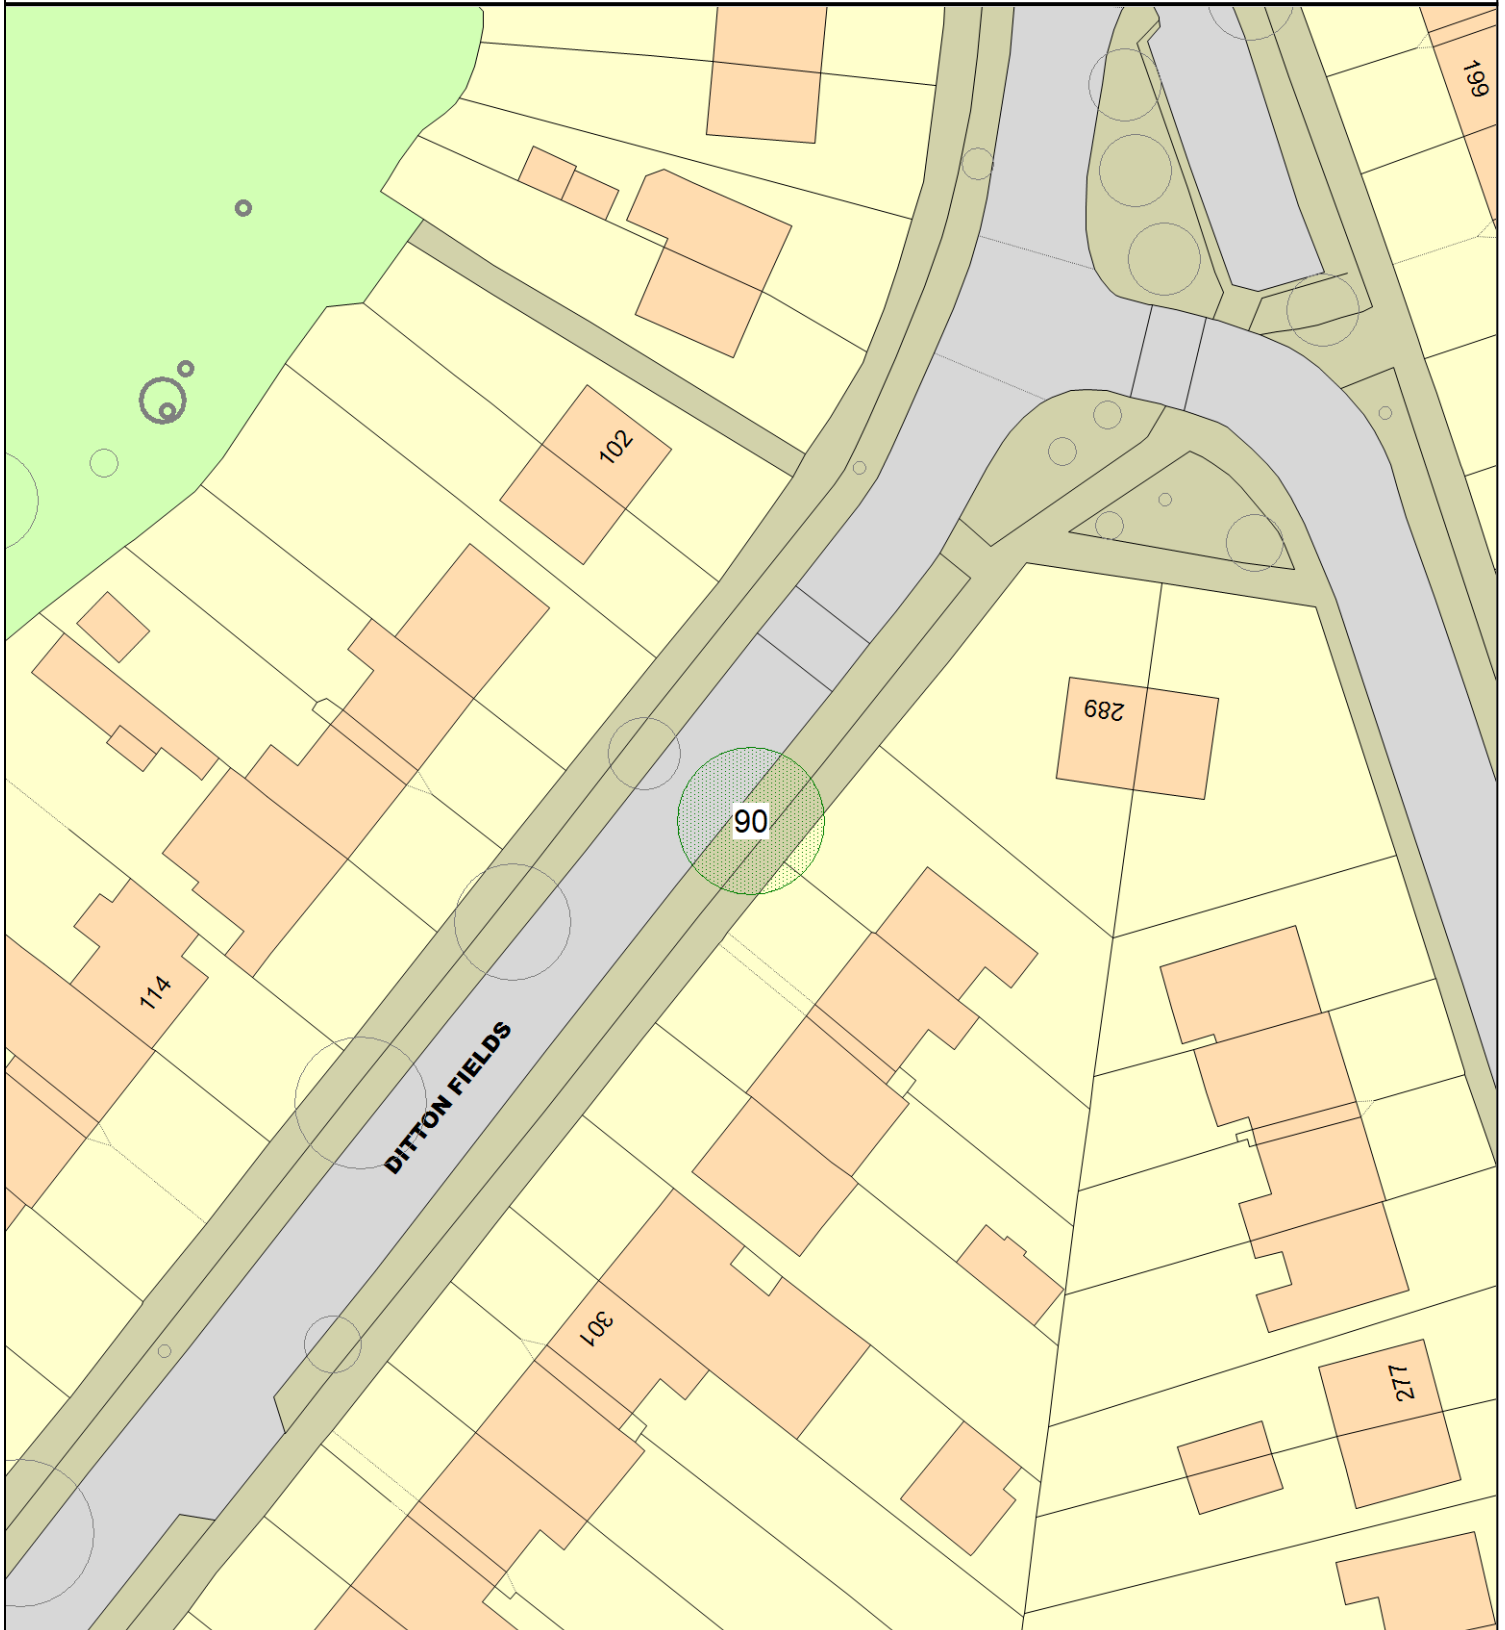



ARBORICULTURAL WORKS ORDER

Item Ref: 02470

Foster Road Allotments (FOSALT), Trumpin



ARBORICULTURAL WORKS ORDER

Item Ref: 02470

High Street, East Chesterton (HIGHSW), E




This map is reproduced from Ordnance Survey material with the permission of Her Majesty's Stationery Office (c) Crown copyright. Unauthorised reproduction infringes Crown copyright and may lead to prosecution or civil proceedings." Cambridge City Council (Licence No. 100019730) 2006.



ARBORICULTURAL WORKS ORDER

Item Ref: 02470

Jack Warren Green Growth Site (JWGGs), A

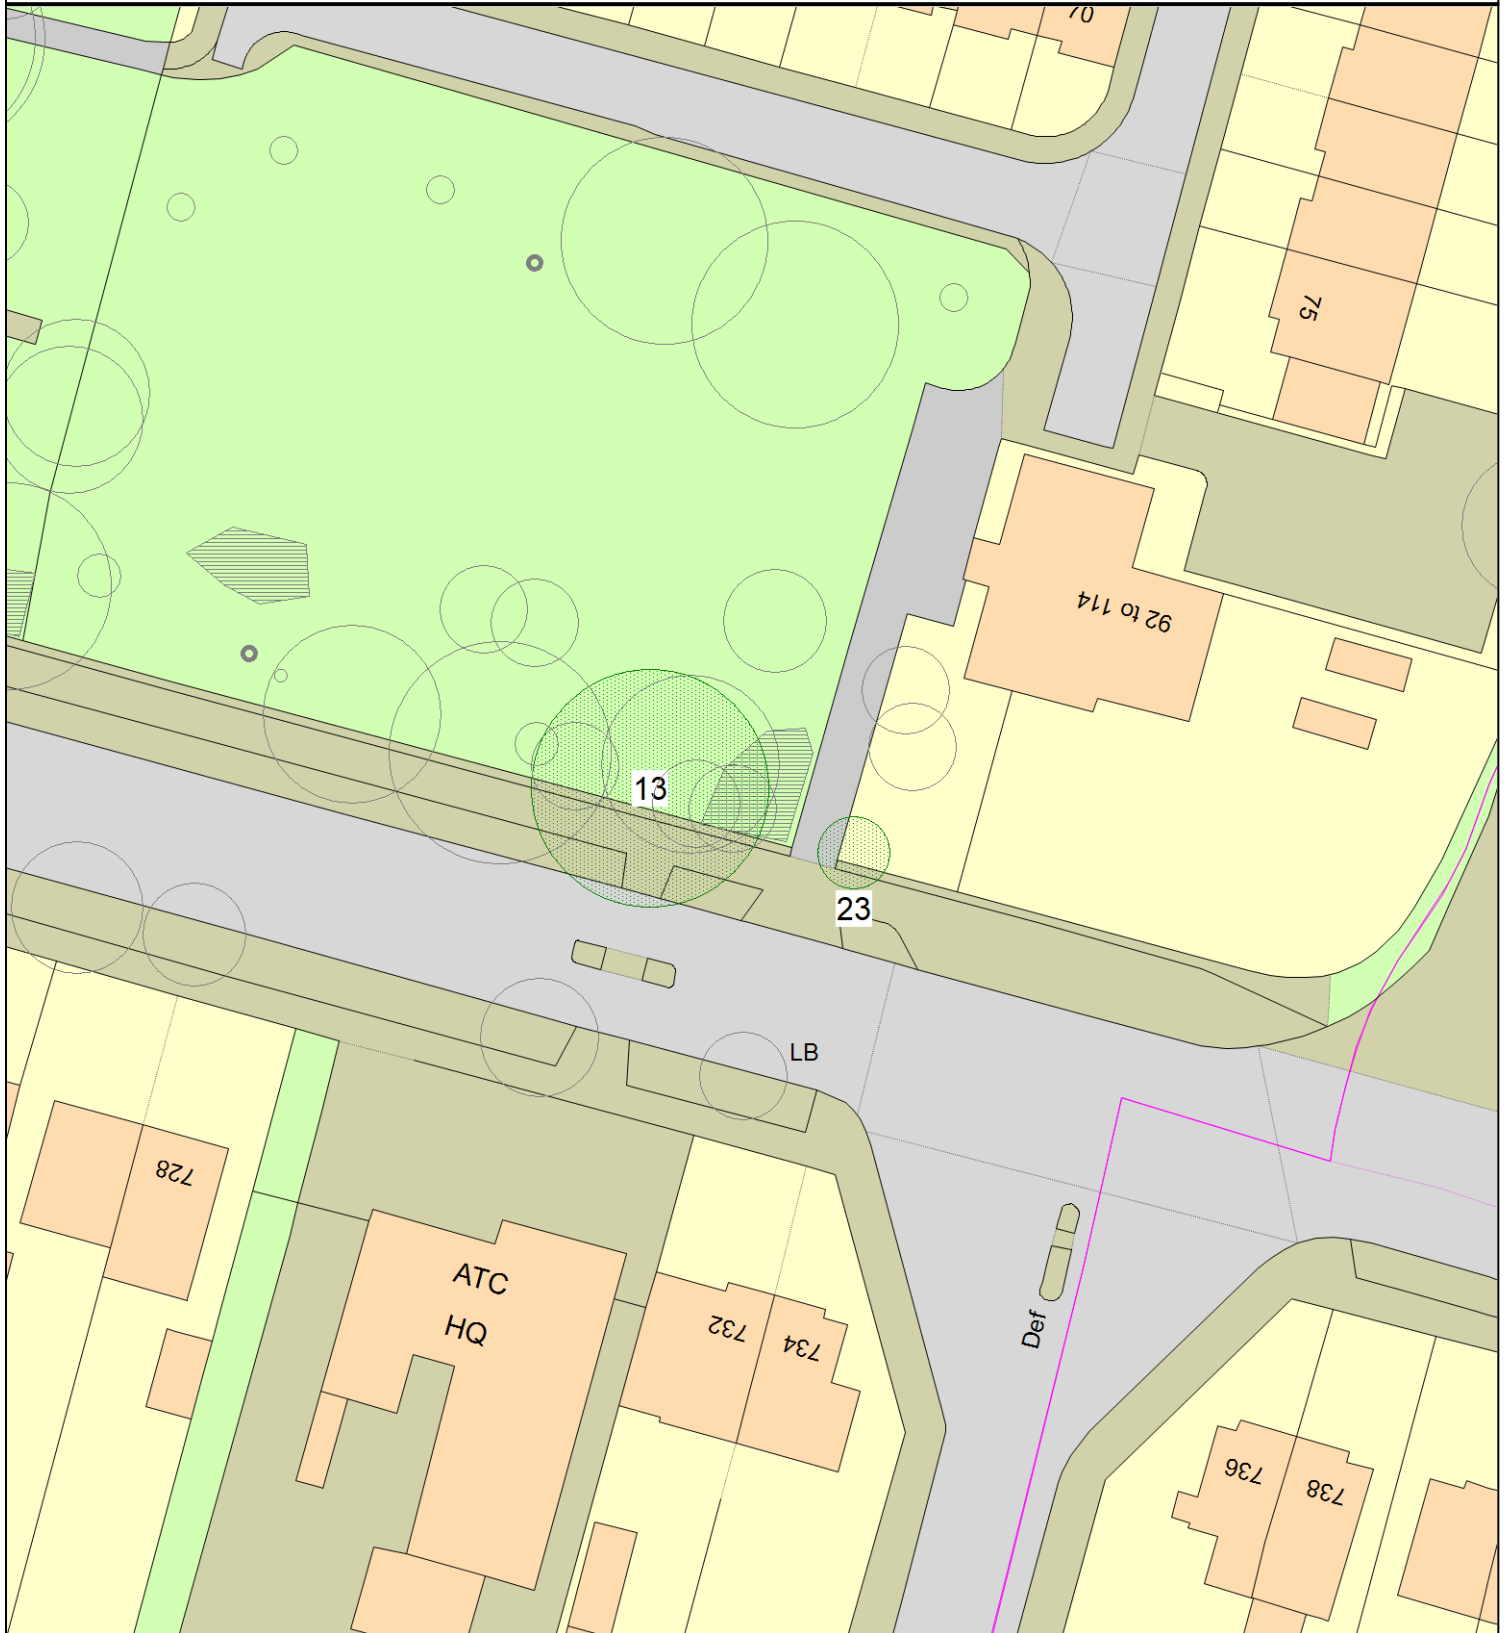

ARBORICULTURAL WORKS ORDER

Item Ref: 02470


Kings Hedges Road (KINGSH), Kings Hedges



ARBORICULTURAL WORKS ORDER

Item Ref: 02470

Monkswell (MONKSW), Trumpington

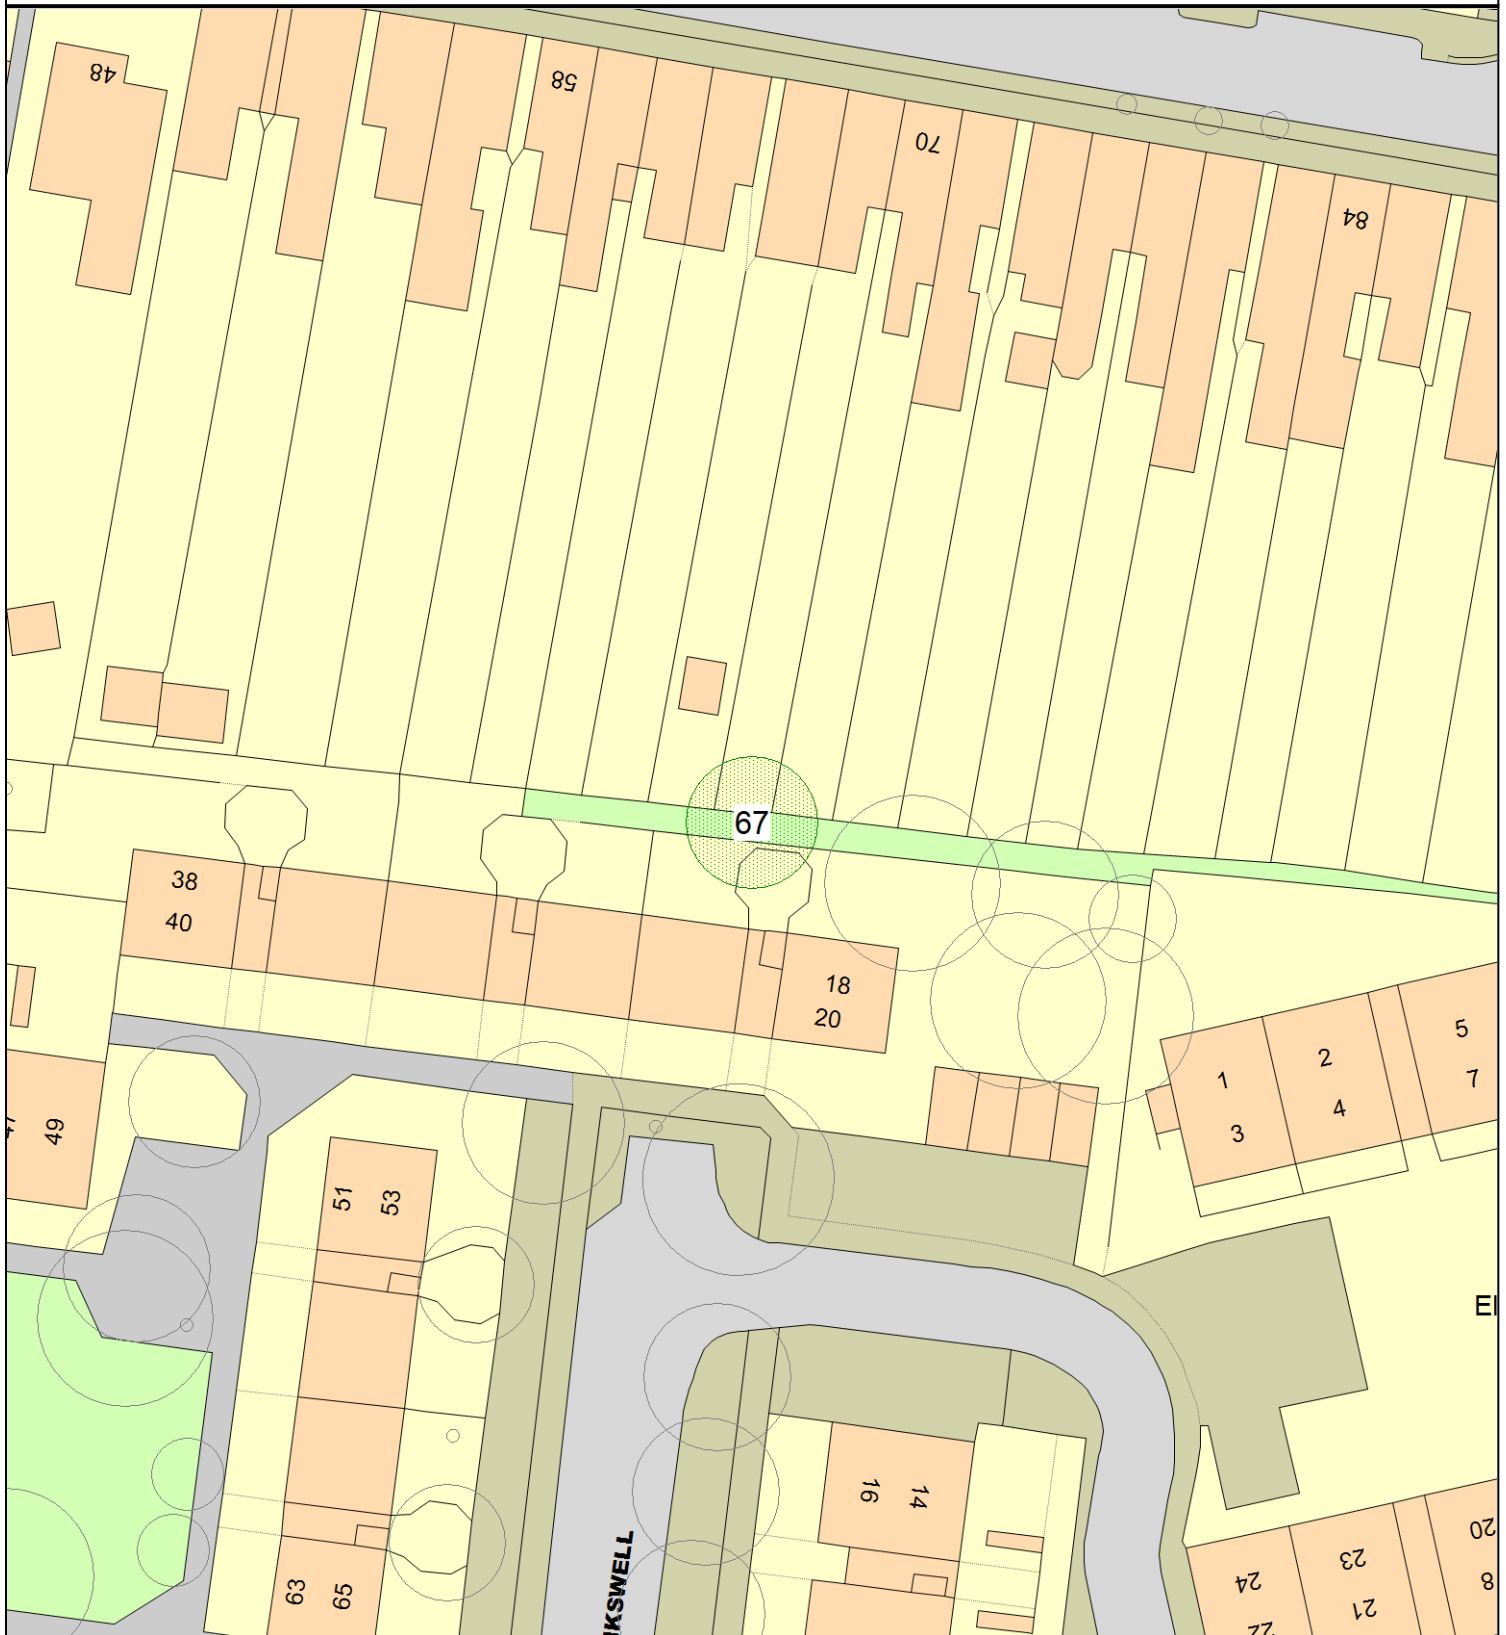

This map is reproduced from Ordnance Survey material with the permission of Her Majesty's Stationery Office (c) Crown copyright.  
Unauthorised reproduction infringes Crown copyright and may lead to prosecution or civil proceedings." Cambridge City Council (Licence No. 100019730)  
2006.


ARBORICULTURAL WORKS ORDER

Item Ref: 02470

Perne Road (PERNER), Coleridge




Peverel Close (PEVERC), Abbey

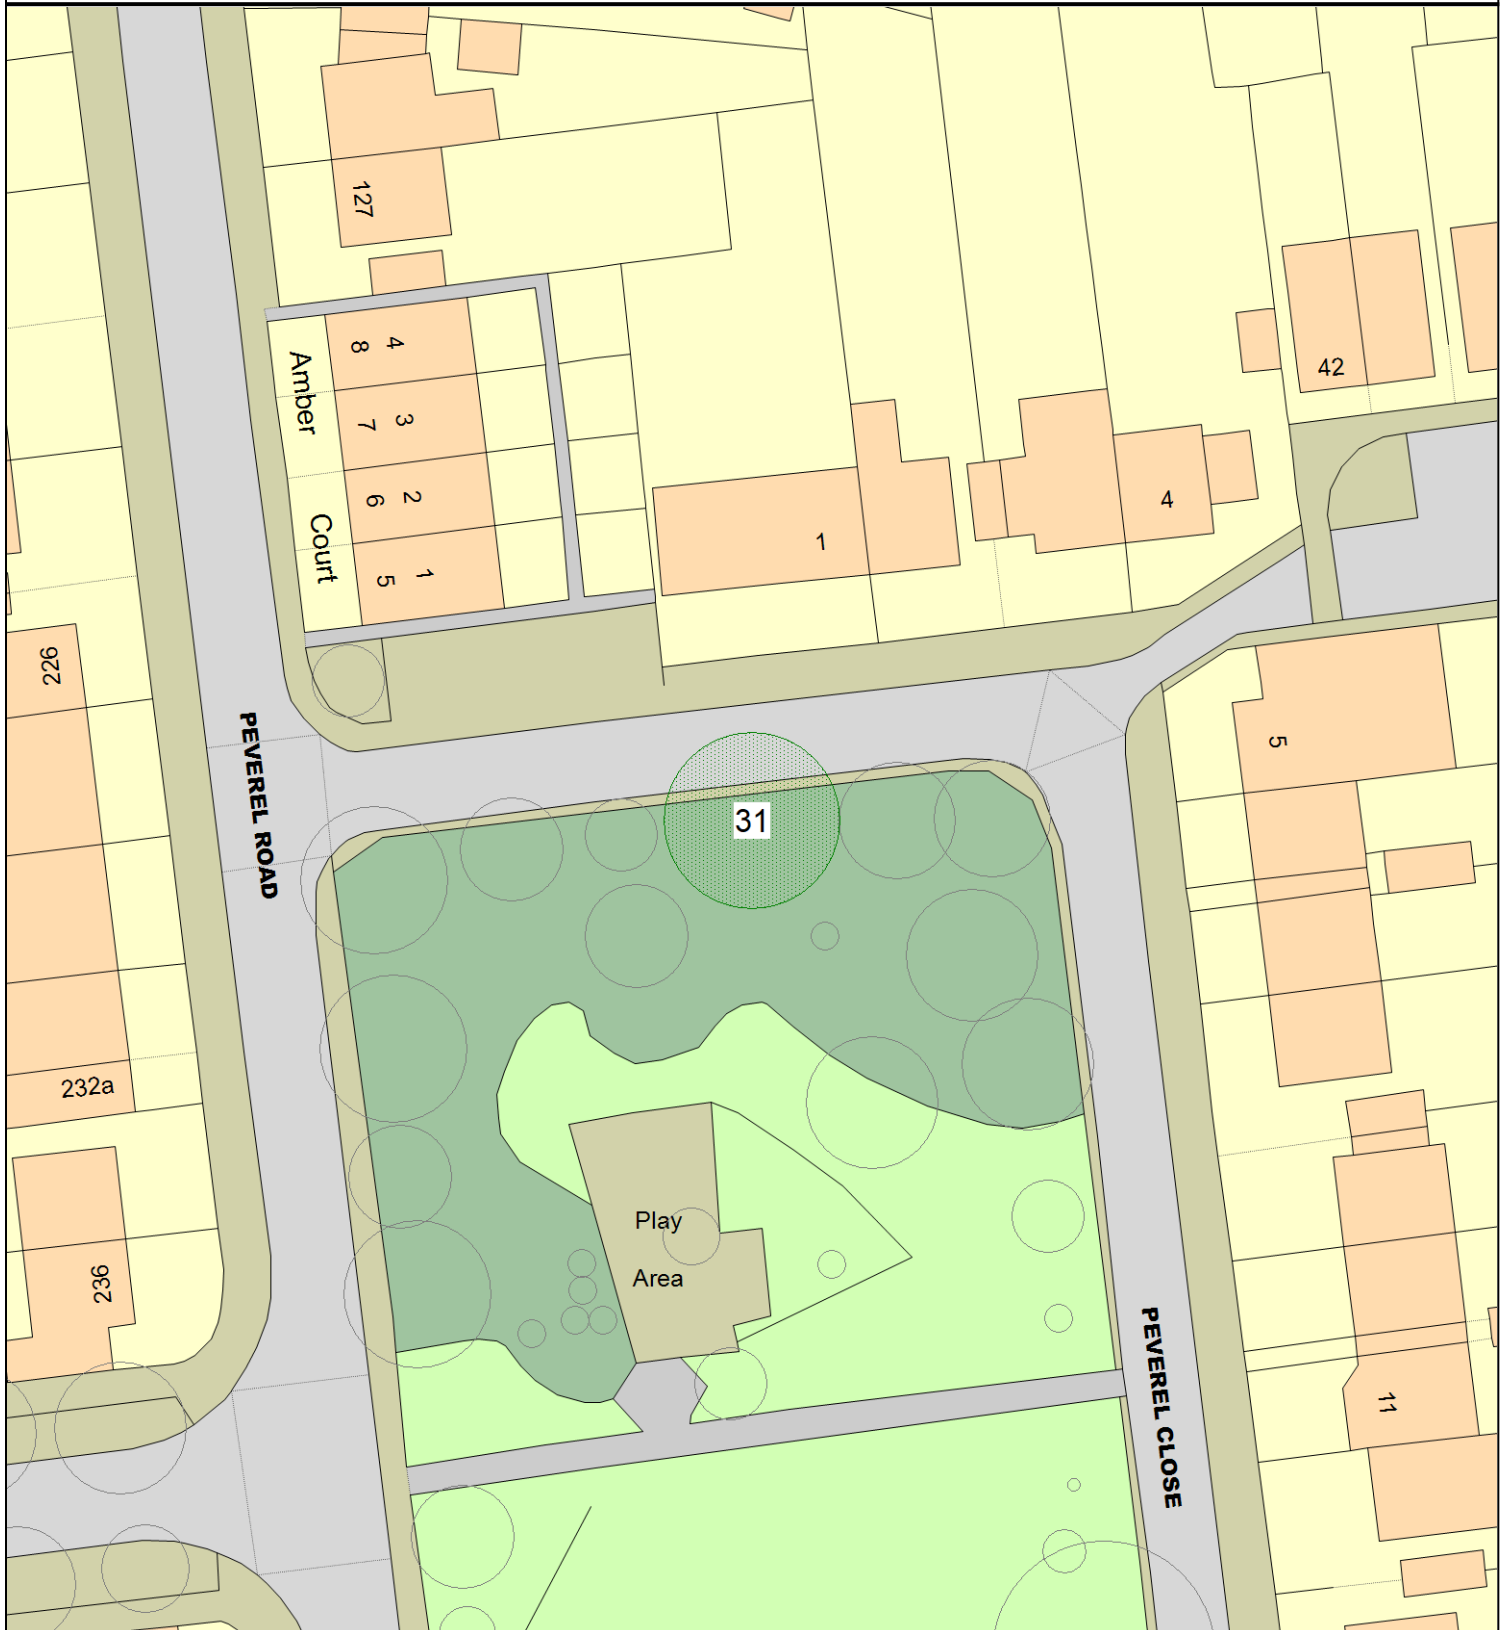

ARBORICULTURAL WORKS ORDER

Item Ref: 02470

Red Cross Lane (REDCRO), Queen Ediths

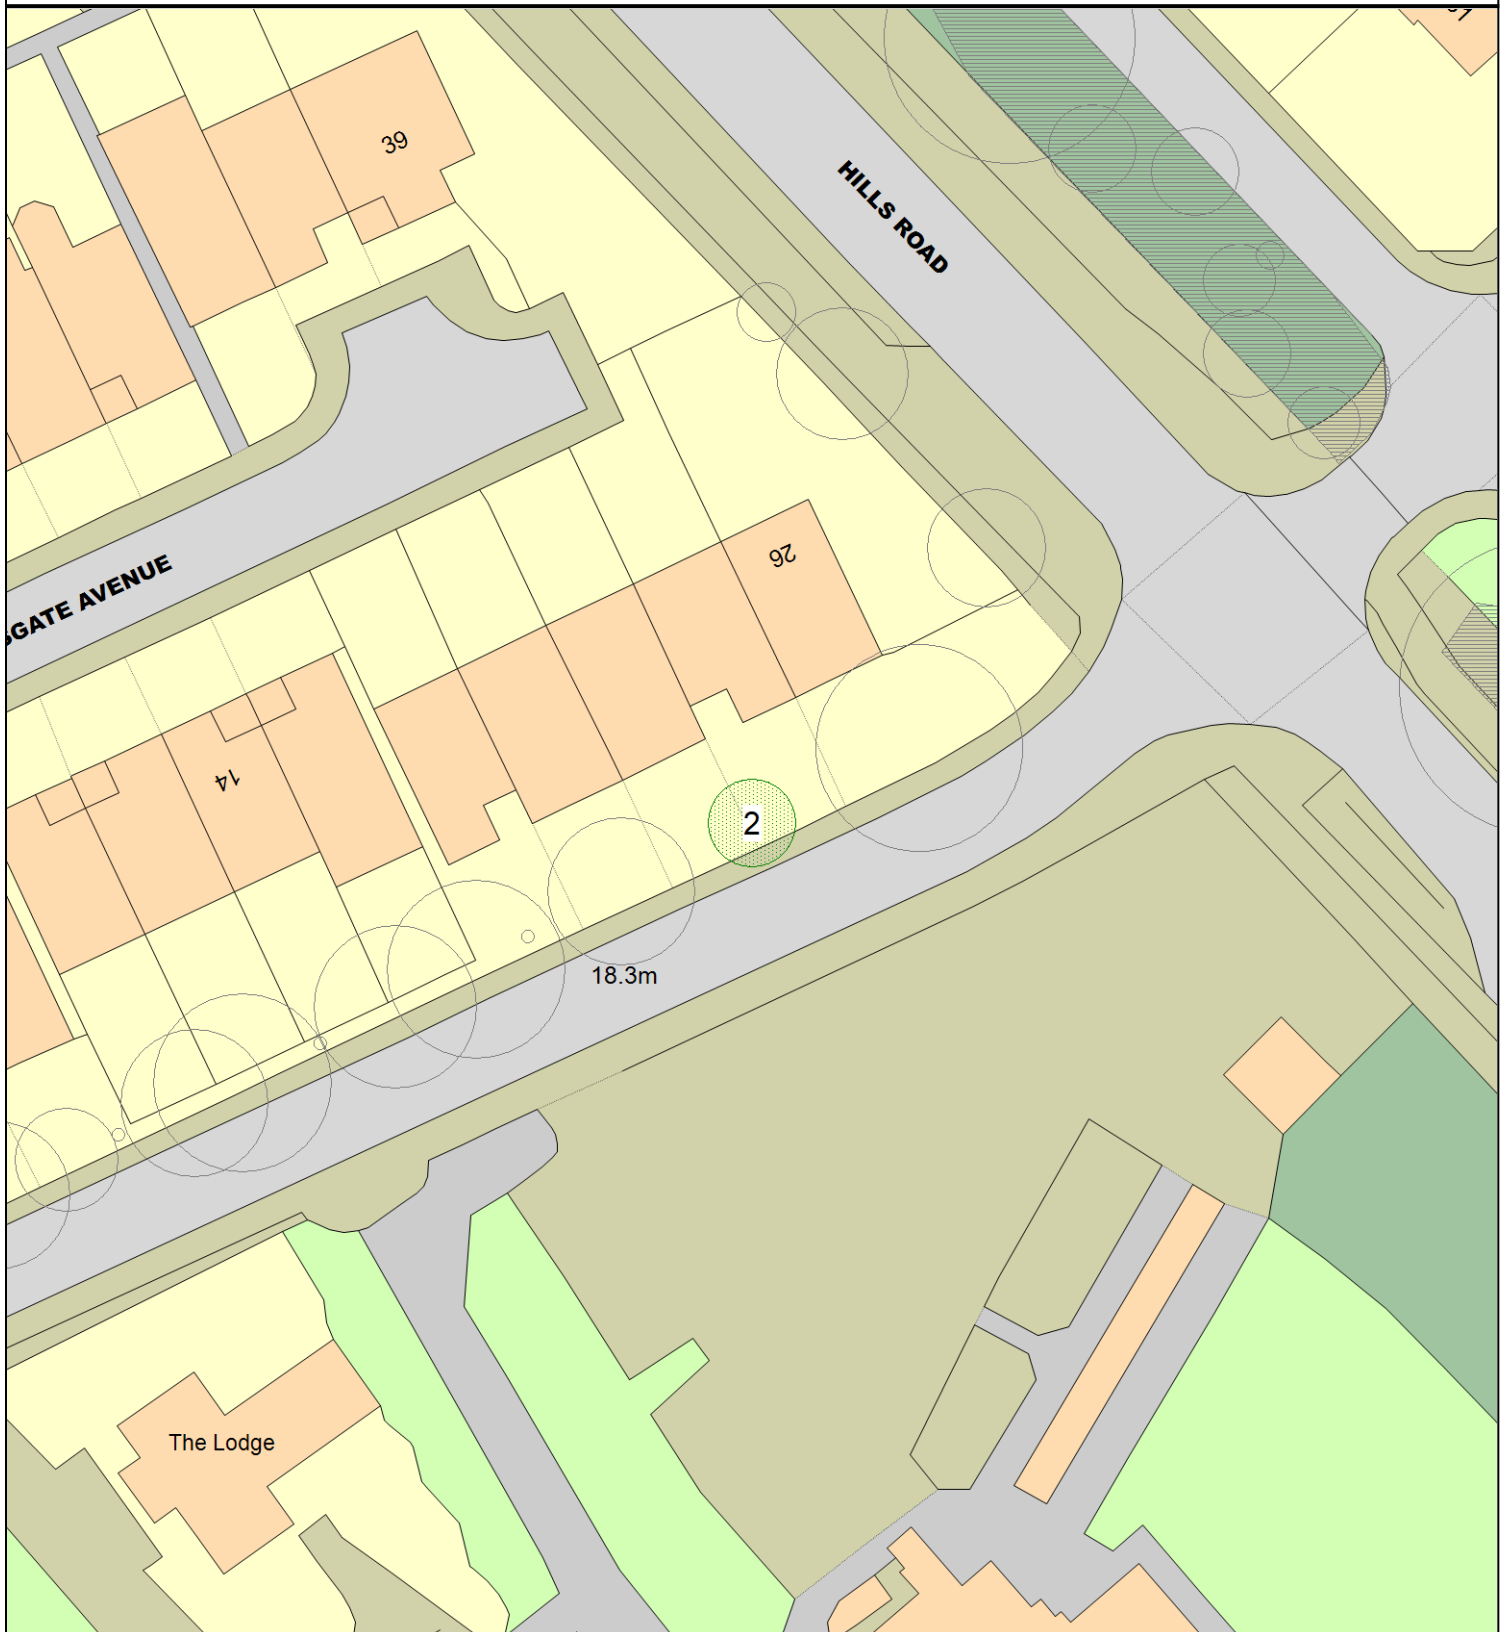




ARBORICULTURAL WORKS ORDER

Item Ref: 02470

Sheeps Green North (COEFEN), Newnham

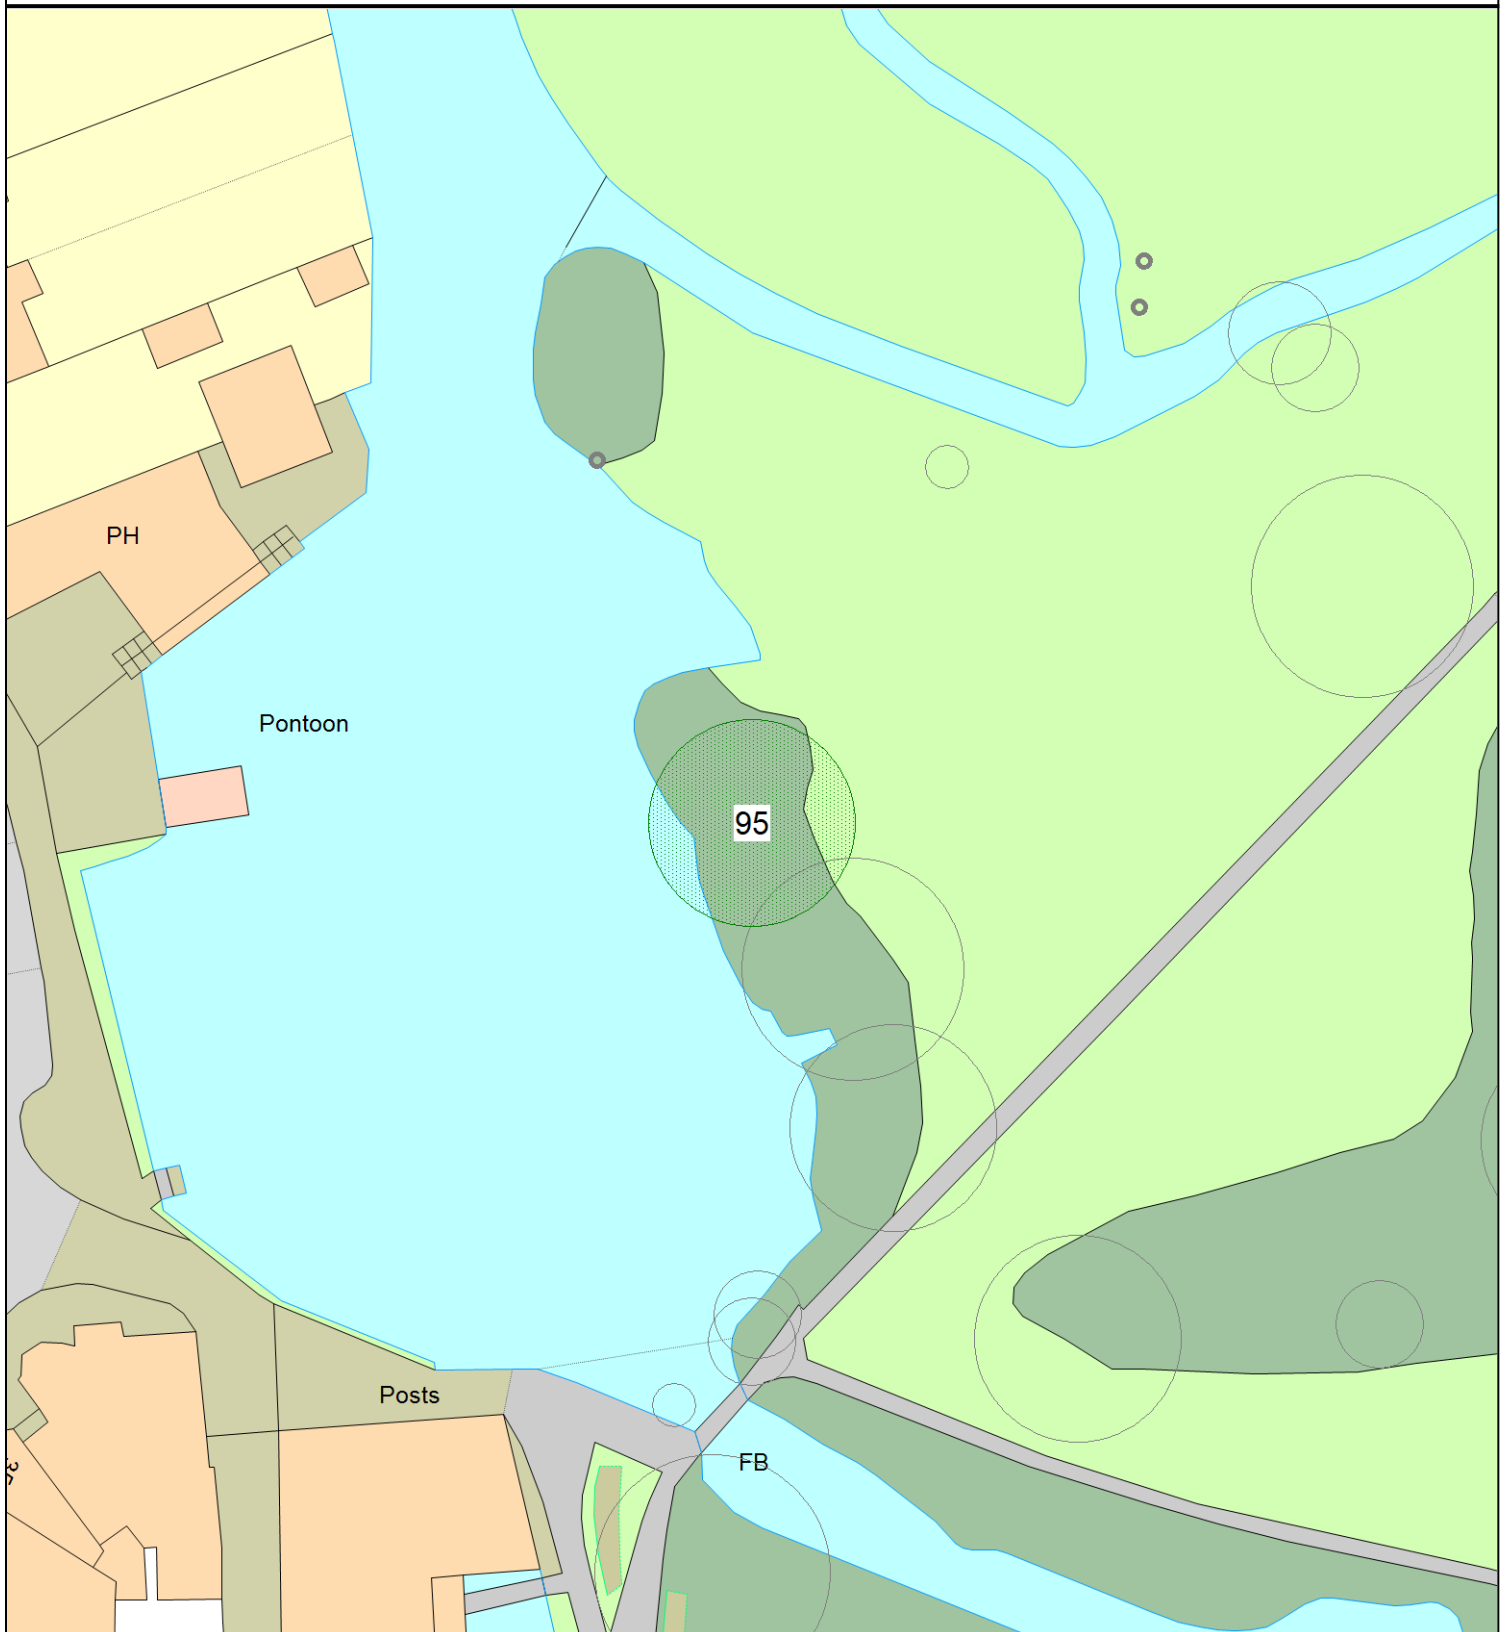




ARBORICULTURAL WORKS ORDER

Item Ref: 02470

Teversham Drift (TEVERE), Cherry Hinton

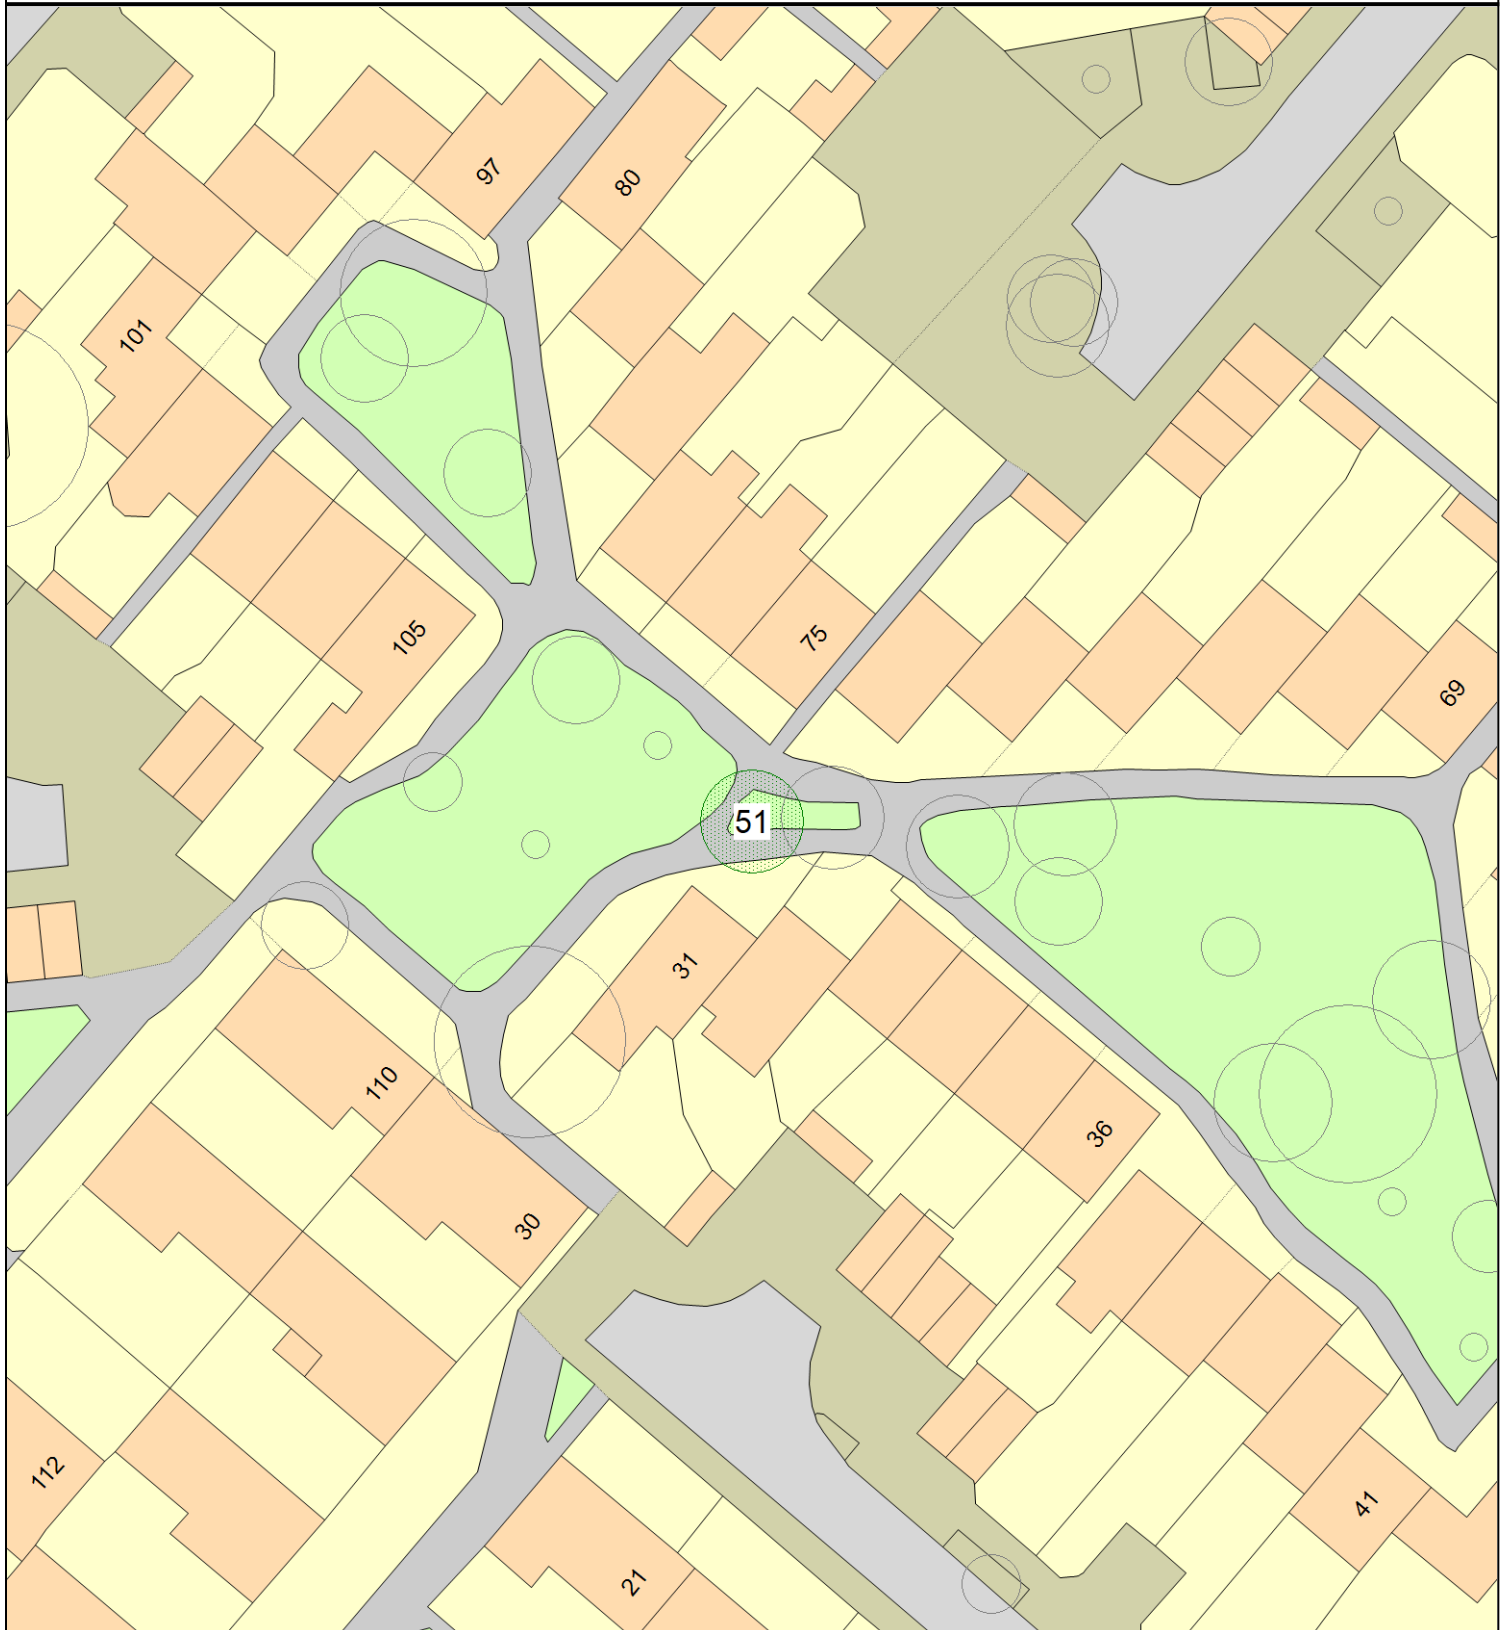

ARBORICULTURAL WORKS ORDER

Item Ref: 02470

Woodlark Road (WOODLR), Castle

